

MOBILE HOME INSTALLERS AFFIDAVIT

Florida Statue Section 320.8249 Requires Mobile Home Installers to be Licensed:

Any person who engages in mobile home installation shall obtain a mobile home installers license from the Bureau of Mobile Home and Recreational Vehicle construction of the Department of Highway Safety and Motor Vehicles Pursuant to this section.

I, _____, License No., _____
Please Type or Print

do hereby state that the installation of the manufactured home at:

911 Address of the Job site

Will be done under my supervision.

Signature

Sworn to and subscribed before me this _____ day of _____ 20_____.

Notary public: _____, My commission Expires: _____
Signature Date

Personally Known: _____

Produce Valid Identification: _____

Stamp or seal _____

PERMIT NUMBER: _____

TORQUE TEST AFFIDAVIT

I, _____, Have personally performed the Torque Test at the following property location:

911 or legal description

Property Owner

I have made the following determination as follows:

Torque Value: _____ Inch pounds _____ FT. Anchors

Signature

License Number

Date

PENETROMETER TEST AFFIDAVIT

I, _____, Have personally performed the penetrometer test at the following property location:

911 or legal description

Property Owner

I have made the following determination:

Soil load bearing capacity: _____, Or assumed 1000 PSF. _____


Signature

License Number

Date

Penetrometer/Torque Test

X _____ Lbs. _____ Lbs. _____ Lbs.
X _____ inch pounds X _____ inch pounds X _____ inch pounds

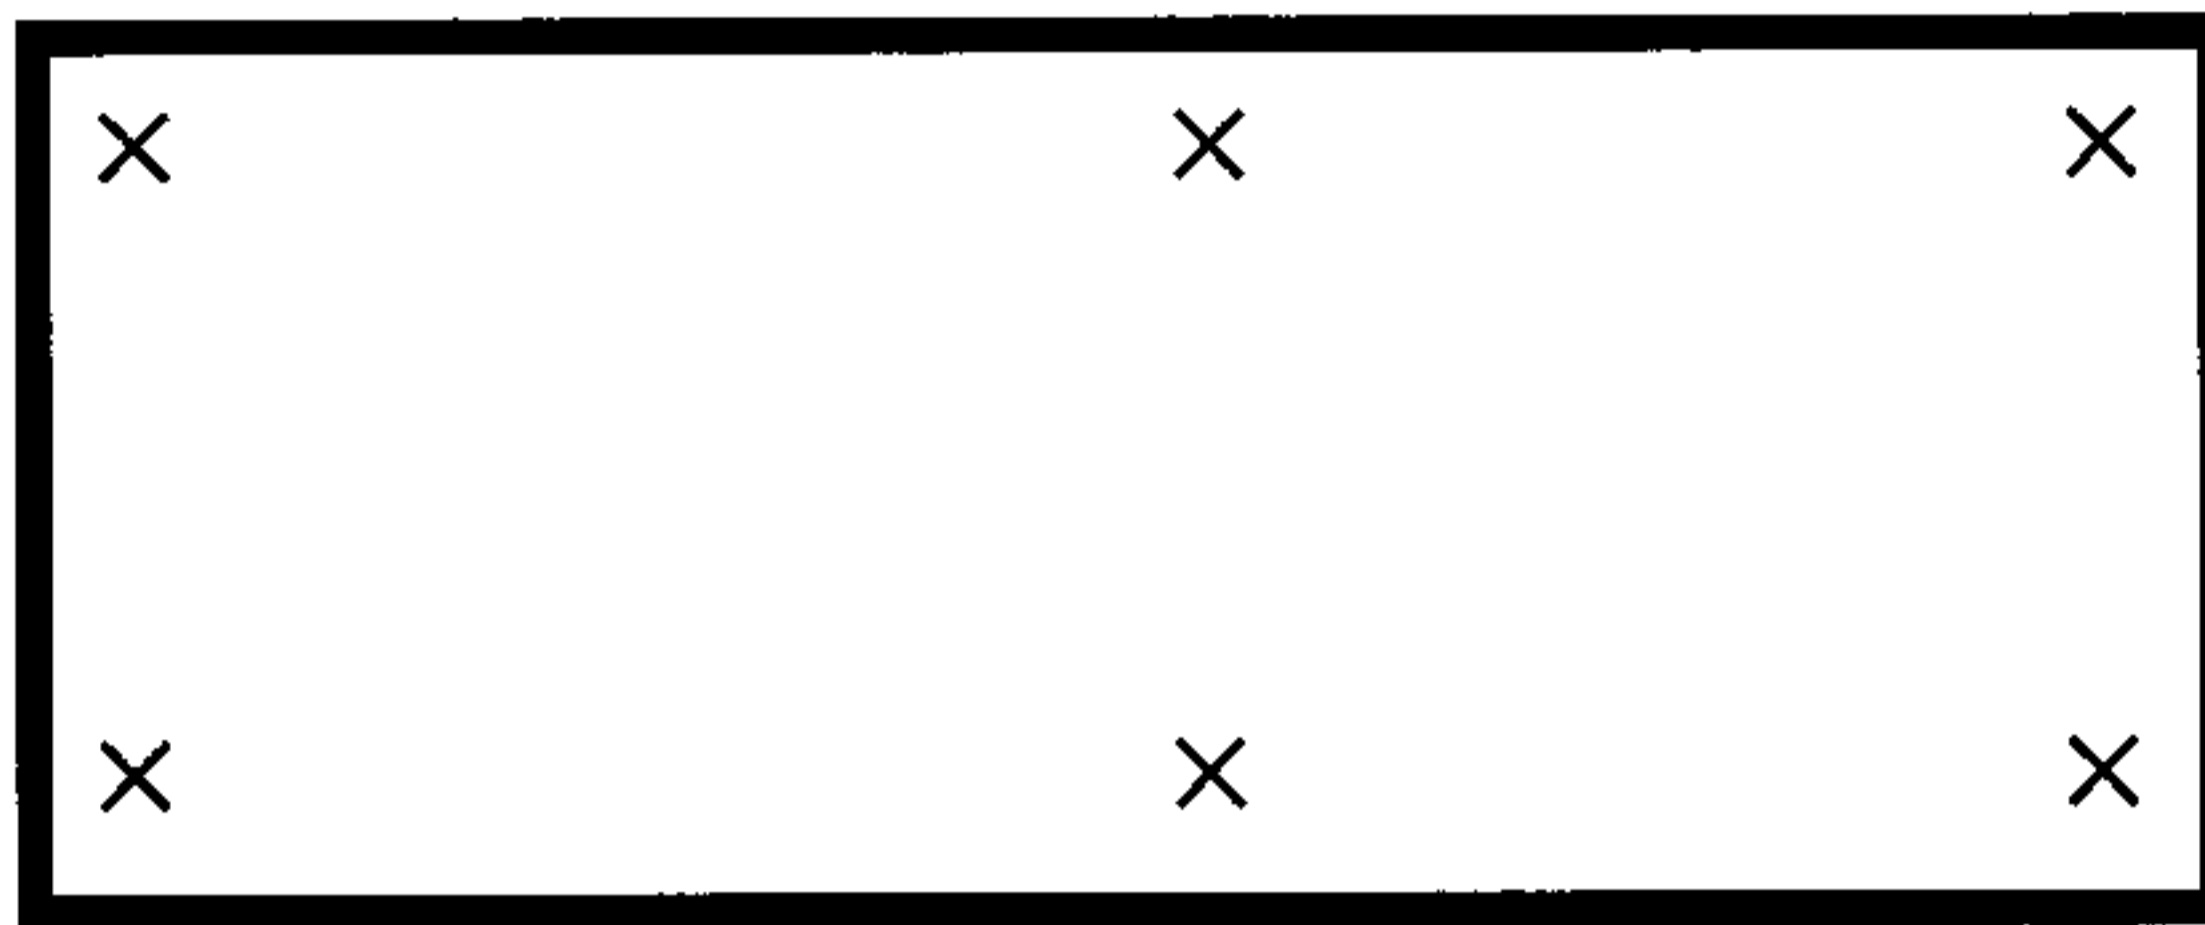

X _____ Lbs. _____ Lbs. _____ Lbs.
X _____ inch pounds X _____ inch pounds X _____ inch pounds

Test the perimeter of the home at six (6) locations

Take the reading at the depth of the footer

Using 500lb. Increment, take the lowest reading and round down to that increment



LEVY COUNTY BUILDING DEPARTMENT
MOBILE/MANUFACTURED HOME SET-UP CERTIFICATION

Property Owner:
Property Owner Address:
Applicant:
Name of Licensed Installer:
Installer's License #:
Installer's Decal#:

Manufacturer's Name:
Number of Sections:
Installation Standard Used: (Check One)
Manufacturer's Manual:
Wind Zone
Serial#

SITE PREPARATION:

Debris and Organic Material Removed
Water Drainage: Natural, Swale, Pad, Other
Compacted Fill
Page #

FOUNDATION:

Load bearing soil capacity:
Footing Type: Poured in place, Portable
I-Beam or Mainrail piers: Single Tiered, Double Interlocked
Size of Piers
Placement O/C
Perimeter Pier Blocking: Yes, No
Ridge Beam Support Footer: Size, Number
Number of Center Line Blocking
Base Size, Location(s)
Special Pier Blocking: Required (Fireplace, Bay Window, Etc) Yes, No
Mating of Multiple Units: Mating Gasket, Type Used
Fasteners: ROOFS Types and Size, Spacing, O/C
ENDWALLS Type and Size, Spacing, O/C
FLOORS Type and Size, Spacing, O/C
Page#

ANCHORS:

Number of Frame Ties: Spacing, O/C, Angle of Strap, Degrees
Number of Centerline Anchors
Number of Stabilizer Devices
Vents Required for Underpinning (1SF/150 SF of Floor Area) Number
Page#

SUBCONTRACTOR'S VERIFICATION MOBILE/MANUFACTURED HOME SET-UP CERTIFICATION

Levy County issues combination permits where one permit covers all trades doing work at one site. It is necessary that we have documentation of the subcontractors who will actually be doing the trade specific work on the mobile home setup.

*Installer:
License#:
SIGNATURE
Print Installer's Name:
Date:

*Plumber:
License#:
SIGNATURE
Print Plumber's Name:
Date:

*Electrician:
License#:
SIGNATURE
Print Electrician's Name:
Date:

*HVAC:
License#:
SIGNATURE
Print HVAC's Name:
Date:
